BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the	Cum	28.24	19.86	70	04-09-2022	11-09-2022	7
2	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the	Cum	40.50	31.95	79	04-09-2022	11-09-2022	7
3	Removing and refixing stone slabs of drains and pointing in CM (1:3) and directions of the Engineer in charge.	Sqm	1168.94	413.35	35	04-09-2022	14-09-2022	10
4	Removing and refixing of footpath slab (Data Rate) and directions of the Engineer in charge.	Sqm	2467.12	1287.41	52	04-09-2022	14-09-2022	10
5	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, key trenches, foundation of bridges and such similar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution lights, removal	Cum	9215.62	4330.43	47	10-09-2022	20-09-2022	10
6	Providing granite slabs of selected quality roughly dressed havieff a size of 7.5cms thick and fixed in cement mortar (1:6) including fixing curing etc., complete and directions of the Engineer in charge. and directions of the Engineer in charge. and directions of the Engineer in charge.	Sqm	191.97	0.00	0	05-09-2022	31-01-2023	148
7	Providing one line dressing to granite stone slab / granite stone masonry as per specifications as directed by the Engineer in Charge of the work. (excluding GST and Area Leading Charges)(Data Rate) and directions of the Engineer in charge. and directions of the Engineer in charge.	Sqm	721.00	413.55	57	24-09-2022	01-10-2022	7
8	Providing and laying in position plain cement concrete Mix 1:3:6 (M10) for levelling course for all works in foundation. Using 40 mm nominal size graded crushed coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150 mm thickness, well	Cum	1511.42	632.31	42	24-09-2022	09-10-2022	15
9	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as	Cum	2146.25	1120.86	52	27-09-2022	18-10-2022	21
10	Supplying, Fitting and Placing TMT Fe550 bar Reinforcement in sub-structure complete as per Drawing and Technical Specifications. and directions of the Engineer in charge.	Tonne	132.87	64.83	49	25-09-2022	08-10-2022	13

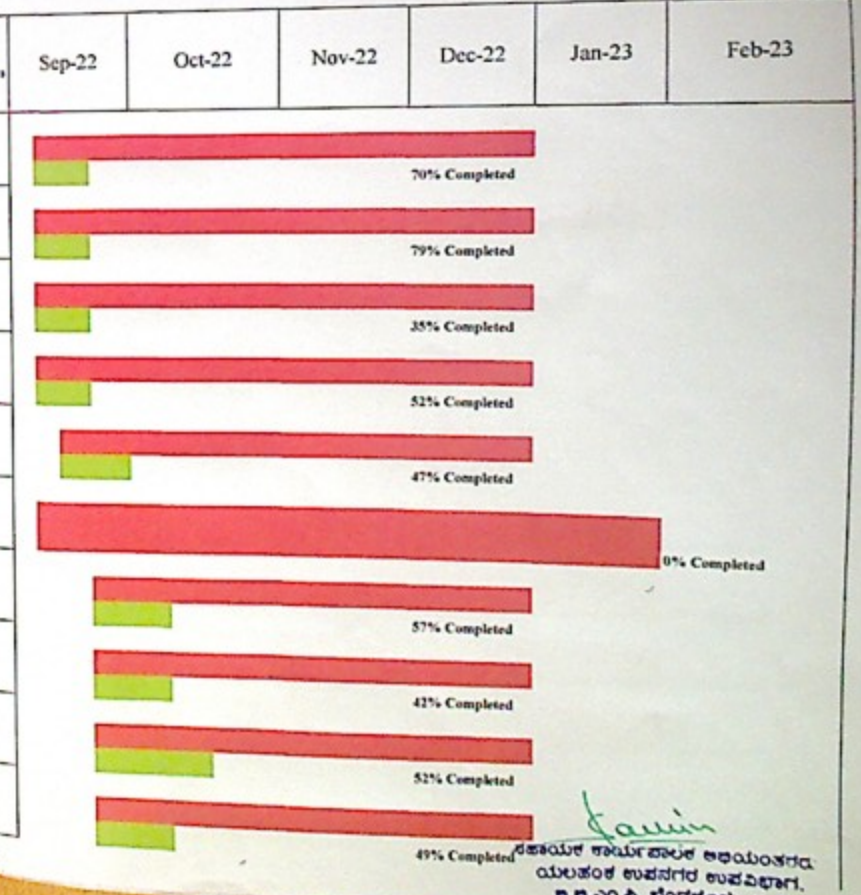

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪವಿಭಾಗ ಉಪವಿಭಾಗ,
ಬ.ಬ.ಮ.ಪ. ಬೆಂಗಳೂರು-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Reehan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
11	Providing and Fixing pre cast covering Slab 100mm thick made out of CC , Jelly 20mm Down Size with steel reinforcement including form work, curing, including cost of all materials, labour, hire charges of machinery, loading, unloading, lead and lift, transportation etc, complete as per	Sqm	5961.71	3029.46	51	30-09-2022	20-10-2022	20
12	Providing and Fixing pre cast covering Slab 150mm thick made out of CC , Jelly 20mm Down Size with steel reinforcement including form work, curing, including cost of all materials, labour, hire charges of machinery, loading, unloading, lead and lift, transportation etc, complete as per	Sqm	289.80	142.74	49	30-09-2022	20-10-2022	20
13	Providing and Fixing pre cast covering Slab 230mm thick made out of CC , Jelly 20mm Down Size with steel reinforcement including form work, curing, including cost of all materials, labour, hire charges of machinery,	Sqm	346.56	74.82	22	30-09-2022	20-10-2022	20
14	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The	Sqm	390.18	146.80	38	02-10-2022	22-10-2022	20
15	Providing and fixing pre cast solid cement concrete Kerb Stones made out of M20 with top and bottom width 114 and 165mm respectively, 406mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour	Cum	19802.00	9005.60	45	02-10-2022	22-10-2022	20
16	Painting Two Coats on New Concrete Surfaces Painting two coats after filling the surface with synthetic enamel paint in all shades on new plastered concretesurfaces. and directions of the Engineer in charge	Sqm	3118.15	0.00	0	05-09-2022	31-01-2023	148
17	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The	Cum	213.14	0.00	0	05-09-2022	31-01-2023	148
18	Providing and laying heavy duty cobble stones 60mm thick interlock pavers, using cement and course sand for manufacture of blocks of approved size, shape and colour with a minimum compressive strength of	Sqm	3772.72	0.00	0	05-09-2022	31-01-2023	148
19	Providing and laying heavy duty cobble stones 75mm thick interlock pavers, using cement and course sand for manufacture of blocks of approved size, shape and colour with a minimum compressive strength of 281 kg per m2	Sqm	1194.40	0.00	0	05-09-2022	31-01-2023	148

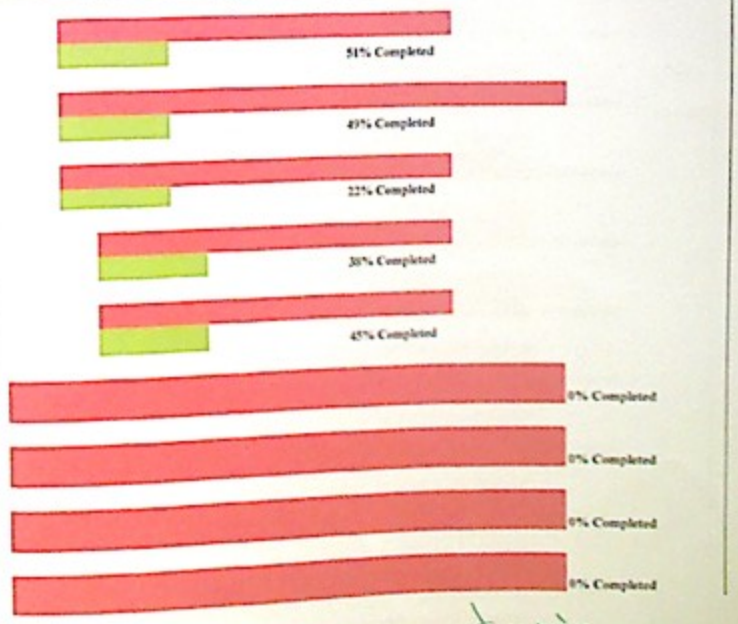

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23
20	Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 m3 in volume and stock piling at designated locations and disposal of dismantled materials and stacking serviceable and unserviceable materials separately MORTH	Cum	535.58	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
21	Earth work in surface excavation by mechanical means for lowering & leveling the ground for all works other than foundation in all kinds of soils & upto depth not exceeding 300mm as per drawing and technical specifications, including setting out, shoring, structure, barricading, caution lights, removal	Cum	3109.42	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
22	Scarifying the existing bituminous road surface to a depth of 50 mm and disposal of scarified material by Mechanical Means using Hydraulic excavator with in all lifts and lead and directions of the Engineer in charge.	Sqm	1353.30	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
23	Construction of Granular Sub-Base of required grading as per design mixing in a mechanical mix plant at OMC, carriage of mixed Material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the desired density.	Cum	206.52	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
24	Providing, laying, spreading and compacting graded stone aggregate to wet mix macadam specification including premixing the Material with water at OMC in mechanical mix plant carriage of mixed Material by tipper to site, laying in uniform layers with motor grader in sub-base /base course on well	Cum	2788.72	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
25	Providing and applying primer coat with SS1 grade Bitumen Emulsion on prepared surface of granular base including cleaning of road surface and spraying primer at the rate of 0.90 kg per m2 using mechanical means Specification and directions of the Engineer in charge.	Sqm	20542.98	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
26	Providing and laying Dense Graded Bituminous Macadam with 40/60 TPH capacity HMP using crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 4.5 per cent by weight of total mix and filler, transporting the hot mix to work site, laying with mechanical paver finisher	Cum	1027.15	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
27	Providing and applying tack coat with RS1 Bituminous Emulsion using emulsion pressure distributor at the rate of 0.25 kg/m2 on the prepared bituminous surface cleaned with mechanical brooms Specification and directions of the Engineer in charge.	Sqm	30511.44	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
28	Providing and laying Bituminous Concrete with 40/60 TPH capacity hot mix plant using crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 5.4 percent of mix and filler, transporting the hot mix to work site, laying with mechanical paver finisher to the required	Cum	1220.46	0.00	0	05-09-2022	31-01-2023	148	0% Completed					
29	Road Marking with Hot Applied Thermoplastic Compound with Reflectorising Glass Beads on Bituminous Surface Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads @ 250 g/ m2 area, thickness of 2.5 mm is exclusive of surface	Sqm	991.18	0.00	0	05-09-2022	31-01-2023	148	0% Completed					

Executive Engineer
Yelahanka

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

	Assigment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
0	for all works in foundation. The granite metal / hand crushed graded course aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150 mm thickness, well consolidated	Cum	585.88	0.00	0	05-09-2022	31-01-2023	148
11	Providing and constructing un-reinforced plain cement concrete pavements, thickness as per design, over a prepared sub base, with 43 grade cement or any other type as per Clause 1501.2.2.M30 (Grade), coarse and fine aggregates conforming to IS 383, maximum size of coarse aggregate not	Cum	524.48	0.00	0	05-09-2022	31-01-2023	148
32	Cutting transverse contraction joints 3 to 4 mm wide and depth 60mm in concrete slab using concrete cutting machine with diamond studded saw within 48 hours of casting of bay / slab etc. complete including subsequent widening of the groove 8 to 10 mm wide at top but not depth of 15 mm as	M	728.00	0.00	0	05-09-2022	31-01-2023	148
33	Providing to contraction joints polysulphide sealent (Pouring grade) confirming to BS 5212 - 1969 into sawed groove widened at top for sealent reservoir of specified size and shape as per detailed drawing including fixing Polyethylene foam backer rod of required diameter	M	728.00	0.00	0	05-09-2022	31-01-2023	148
34	Providing and applying Epoxy paint of approved quality over newly laid cement concrete surface for cycle track with 2coats of primer (@0.35kg/Sqm) one mid coat sprayed at 2.1kg per sqm mixed with m Sand at 3.15kg per Sqm and top coat sprayed at 0.35kg per Sqm along with	Sqm	3000.00	2047.43	68	10-09-2022	15-09-2022	5
35	Demolishing brick work manually/ by mechanical means including stacking of serviceable material and disposal of unserviceable material to the appropriate disposal area as per direction of Engineer-in-charge in Cement mortar	Sqm	15.60	15.60	100	10-09-2022	15-09-2022	5
36	Dismantling tile work in floors and roofs laid in cement mortar including stacking material to the appropriate disposal area as per direction of Engineer-in-charge. For thickness of tiles 10 mm to 25 mm	Sqm	28.44	28.44	100	10-09-2022	15-09-2022	5
37	Demolishing R C C work manually by mechanical means including stacking of steel bars and disposal of unserviceable material to the appropriate disposal area as per direction of Engineer-in -charge	Sqm	5.75	5.75	100	10-09-2022	15-09-2022	5
38	Earth work excavation for Foundation by mechanical means for all works & depth upto 3 m, as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution lights, including dressing of excavated surfaces, disposing off or leveling the excavated earth or	Cum	123.45	122.17	99	10-09-2022	15-09-2022	5

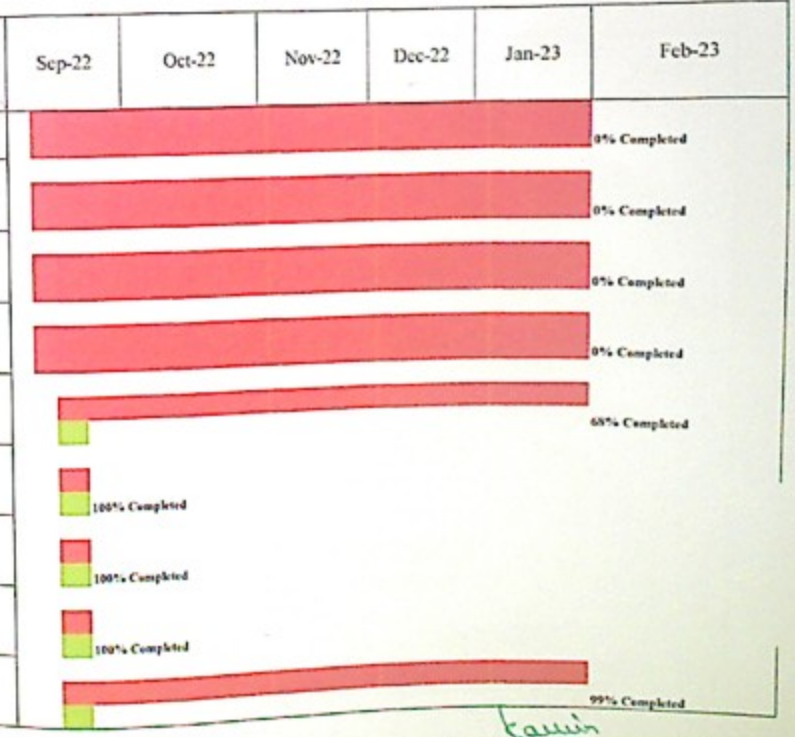

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
39	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, Key trenches, foundation of bridges and such simullar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution lights, removal of stumps and other deleterious matter. excavated surface	Cum	561.59	20.91	4	10-09-2022	15-09-2022	5
40	Providing and Filling in foundation with granite / trap broken metal 100mm and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. complete as per specifications.	Cum	109.21	26.62	24	12-09-2022	19-09-2022	7
41	Filling available excavated earth (excluding rock) in trenches, plinth, sides of foundations and other simular works etc in layers not exceeding 20cm in depth, consolidating each deposited layer by ramming and watering, lead up to 50 m and lift upto 1.5 m.	Cum	239.60	16.87	7	14-09-2022	21-09-2022	7
42	Providing Size Stone masonry with hard stone in foundation & plinth with Cement mortar 1:6 (1 cement : 6 coarse sand)	Cum	354.36	83.38	24	17-09-2022	27-09-2022	10
43	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers, laid in	Cum	3.91	3.86	99	29-10-2022	04-11-2022	6

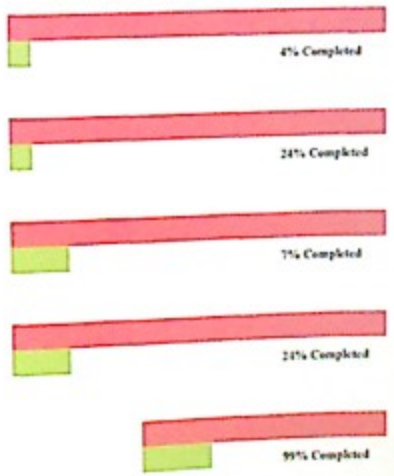

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಾರ್ಯಾಲಯದ
ಮುದ್ರೆಯ ಉಪಯೋಗದ ಉಸ್ತುವಾರಿ,
ಬ ಬ ಮ ಪಾ. ಯಲಹಂಕ-10

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
44	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming	Cum	94.28	10.74	11	16-11-2022	23-11-2022	7
45	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming	Cum	44.88	0.53	1	19-11-2022	23-11-2022	4
46	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming	Cum	2.47	0.00	0	05-09-2022	31-01-2023	148
47	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	6.48	0.00	0	05-09-2022	31-01-2023	148
48	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	57.10	0.00	0	05-09-2022	31-01-2023	148
49	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	0.18	0.00	0	05-09-2022	31-01-2023	148

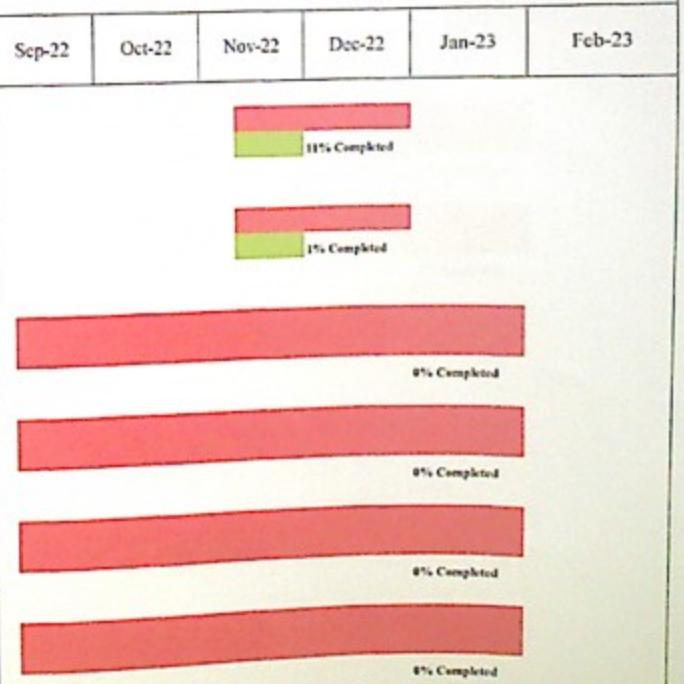

Executive Engineer (Electrical)
Bruhat Bengaluru Mahanagara Palike
B.B.M.P. Yelahanka-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Reehan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assigament	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
50	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	6.21	0.00	0	05-09-2022	31-01-2023	148
51	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	25.85	0.00	0	05-09-2022	31-01-2023	148
52	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	2.05	0.00	0	05-09-2022	31-01-2023	148
53	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/ basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers laid in layers, well compacted	Cum	0.86	0.00	0	05-09-2022	31-01-2023	148
54	Providing Thermo-Mechanically Treated bars of grade Fe-550 Steel reinforcement for R.C.C work including straightening, cutting, bending, placing in position, binding and anchoring to adjacent members wherever necessary complete as per Design including cost of material, labour, usage charges complete as per specifications. (The laps and wastages shall not be	kg	29899.49	1481.06	5	29-10-2022	19-11-2022	21
55	Providing Thermo-Mechanically Treated bars of grade Fe-550 Steel reinforcement for R.C.C work including straightening, cutting, bending, placing in position, binding and anchoring to adjacent members wherever necessary complete as per Design including cost of material, labour, usage charges complete as per specifications. (The laps and wastages shall not be	kg	4888.43	0.00	0	05-09-2022	31-01-2023	148

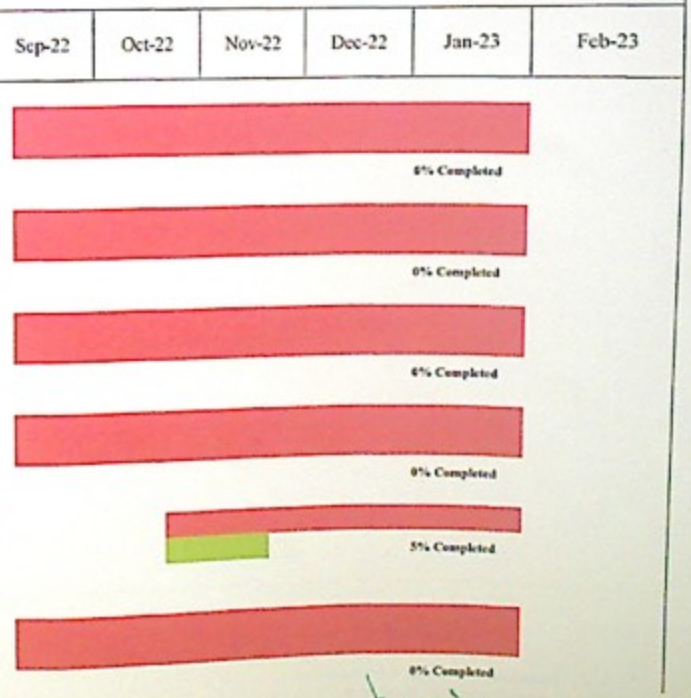

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ ಯಲಹಂಕ,
ಬ.ಬ.ಮ.ಪ. ಬೆಂಗಳೂರು-೫೬

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
56	Providing Tile brick masonry with common burnt clay Non Modular tile bricks of class designation 5.0 conforming to IS 2690 (Part I) in superstructure above plinth level up to floor II level in cement mortar 1:6 (1 cement : 6 coarse sand) including cost of all materials, labour, scaffolding and usage charges of machinery & other incidental charges complete and as	Sqm	114.00	0.00	0	05-09-2022	31-01-2023	148
57	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x150x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572 2005 including cost of all materials, labour, scaffolding and curing, usage	Sqm	0.34	0.00	0	05-09-2022	31-01-2023	148
58	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x150x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572 2005 including cost of all materials, labour, scaffolding and curing, usage	Sqm	128.89	0.00	0	05-09-2022	31-01-2023	148
59	Applying stamping finish on M30 grade concrete on PCC sub grade, applying and finishing with stamp/ stencil of approved pattern and color in accordance with Engineers instructions & approved drawings with use of any approved brand of color hardener of 4.5 kg/m2, including floating of color hardener over the concrete surface with different types of floaters,	Sqm	29.35	0.00	0	05-09-2022	31-01-2023	148
60	Providing and laying water proofing treatment to the Roof with PU based single component elastomeric pure polyurethane based coating on New terrace/Chajja/Sunken portion of WC Bathroom, cold applied PU waterproofing membrane that is highly elastic with elongation greater than 400% and tensile strength greater than 2MPa as per ASTM D412. The	Sqm	165.67	59.37	36	19-11-2022	26-11-2022	7

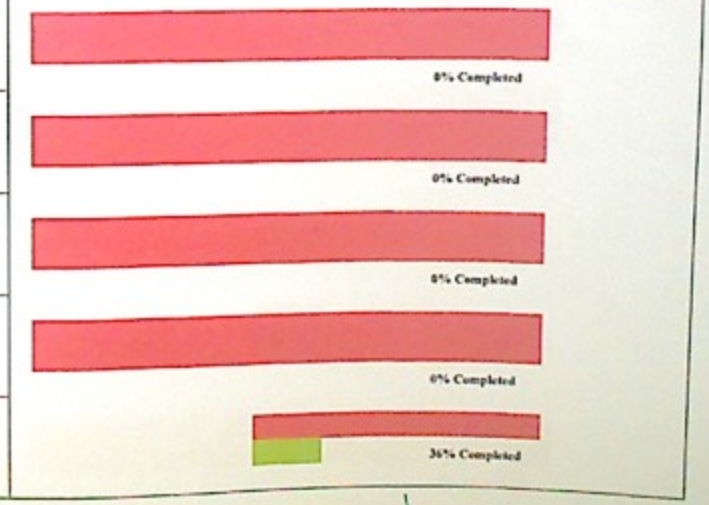

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
61	Providing and laying 52 mm thick cement concrete flooring with concrete hardener topping, under layer 40 mm thick cement concrete 1:2:4 (1cement 2 course sand 4 graded stone aggregate 20 mm nominal size) and top layer 12 mm thick cement hardener consisting of mix 1:2(1 cement hardener mix 2 graded stone aggregate 6 mm nominal size) by volume, hardening	Sqm	29.35	0.00	0	05-09-2022	31-01-2023	148
62	Providing and laying 52 mm thick cement concrete flooring with concrete hardener topping, under layer 40 mm thick cement concrete 1:2:4 (1cement 2 course sand 4 graded stone aggregate 20 mm nominal size) and top layer 12 mm thick cement hardener consisting of mix 1:2(1 cement hardener mix 2 graded stone aggregate 6 mm nominal size) by volume, hardening	Sqm	94.52	0.00	0	05-09-2022	31-01-2023	148
63	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x200x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572 2005 including cost of all materials, labour, scaffolding and curing, usage charges of machinery etc	Sqm	515.47	593.04	100	19-11-2022	26-11-2022	7
64	Providing 20 mm cement plaster of mix 1:4 (1 cement: 4 fine sand) to brick/stone masonary including rounding off corners wherever required smooth rendering, providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications and as per the direction of engineer incharge of work.	Sqm	874.16	930.31	100	19-11-2022	26-11-2022	7
65	Providing 20 mm cement plaster of mix 1:4 (1 cement 4 fine sand) to brick/stone masonary including rounding off corners wherever required smooth rendering, providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications and as per the direction of engineer incharge of work.	Sqm	153.64	0.00	0	05-09-2022	31-01-2023	148
66	Providing 18 mm cement plaster in two coats under layer 12 mm thick cement plaster with cement mortar 1:5 (1 cement 5 course sand) and a top layer 6 mm thick cement plaster with cement mortar 1:3 (1 cement 3 course sand) finished rough with sponge to brick masonry including rounding off corners wherever required smooth rendering, providing and removing	Sqm	657.75	79.39	12	19-11-2022	26-11-2022	7
67	Providing 18 mm cement plaster in two coats under layer 12 mm thick cement plaster with cement mortar 1:5 (1 cement 5 course sand) and a top layer 6 mm thick cement plaster with cement mortar 1:3 (1 cement 3 course sand) finished rough with sponge to brick masonry including rounding off corners wherever required smooth rendering, providing and removing	Sqm	326.76	0.00	0	05-09-2022	31-01-2023	148

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
68	Painting with synthetic enamel paint of approved brand and manufacture to give an even shade Two coats on new work after thoroughly brooming the surface to remove all dirt, dust, mortar drops and foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour complete as per specifications and as per directions of Engineer-in-charge	Sqm	1476.02	79.39	5	19-11-2022	26-11-2022	7
69	Providing and applying white cement based putty of average thickness 1 mm, of approved brand and manufacturer, over the plastered wall surface to prepare the surface even and smooth complete as per specifications and as per directions of Engineer in charge	Sqm	1026.02	79.39	8	19-11-2022	26-11-2022	7
70	Finishing walls with water proofing cement paint of required shade New work (Two coats applied @ 4.84 kg/10 m²) to give an even shade after thoroughly brooming the surface to remove all dirt, dust, mortar drops and foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour complete as per specifications and as per directions	Sqm	889.94	930.31	105	19-11-2022	26-11-2022	7
71	Finishing walls with water proofing cement paint of required shade New work (Two coats applied @ 4.84 kg/10 m²) to give an even shade after thoroughly brooming the surface to remove all dirt, dust, mortar drops and foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour complete as per specifications and as per directions	Sqm	153.64	0.00	0	05-09-2022	31-01-2023	148
72	Providing and laying vitrified floor tiles in different sizes (thickness to be specified by the manufacturer) with water absorption less than 0.08% and conforming to IS: 15622, of approved make, in all colours and shades, laid on 20mm thick cement mortar 1:4 (1 cement : 4 coarse sand), jointing with grey cement slurry @ 3.3 kg/ m2 including grouting the joints with white cement	Sqm	37.10	46.38	125	19-11-2022	26-11-2022	7
73	Providing and fixing flush door shutter made out of solid core block board type, well seasoned , chemicaly treated hard wood battens and internal frame with minimum 45 mm wide wooden frame around door shutters covered with cross bonded wooden sheets (core veneer) hot pressed and fastened on both sides of the door useing liquid phenol formaldehyde resin as per IS	Sqm	1.89	1.89	100	19-11-2022	26-11-2022	7

ಯಲಹಂಕ ಉಪವಿಭಾಗ ಉಪವಿಭಾಗ
ಜ ಜ ಪಾ.ಸ. ಬೆಂಗಳೂರು-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23
74	Providing Salwood frames of doors, windows, clerestory windows, ventilators and other frames, wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and tide clamps), but including cost of materials, labour, usage charges complete as per specifications and as per the direction of engineer incharge of work	Cum	0.04	0.04	95	19-11-2022	26-11-2022	7			95% Completed			
75	Providing & fixing of 3-track x 2-panel sliding windows made out of multi chambered UPVC(Matching to RAL-9016) sections and with minimum TiO2(Titanium Dioxide) at 6PHR with TPE(Thermo Plastic Elastomer) and lead free, gaskets -grey colour having isolated drainage and reinforced with Galvanized Iron profile through-out the window frame. The outer frame	Sqm	4.20	2.61	62	19-11-2022	26-11-2022	7			62% Completed			

Executive Engineer
Division Executive Engineer,
Yelahanka-106

BRUHAT BENGALURU MAHANAGARA PALIKE

lients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
76	Providing & fixing of 3-track x 2-panel sliding windows made out of multi chambered UPVC(Matching to RAL-9016) sections and with minimum TiO2(Titanium Dioxide) at 6PHR with TPE(Thermo Plastic Elastomer) and lead free, gaskets -grey colour having isolated drainage and reinforced with Galvanized Iron profile through-out the window frame. The outer frame	Sqm	23.04	0.00	0	05-09-2022	31-01-2023	148
77	Providing and fixing M.S. grills of required pattern in frames of windows etc with M.S. flats, square or round bars etc. including priming coat with approvedsteel primer all complete. Fixed to openings / wooden frames with rawl plugs screws etc. and as per the direction of engineer incharge of work	Kg	844.20	54.81	6	19-11-2022	26-11-2022	7
78	Providing and fixing M.S. grills of required pattern in frames of windows etc with M.S. flats, square or round bars etc. including priming coat with approvedsteel primer all complete. Fixed to openings / wooden frames with rawl plugs screws etc. and as per the direction of engineer incharge of work	Kg	483.84	0.00	0	05-09-2022	31-01-2023	148
79	Painting Steel work with Deluxe Multi Surface Paint to give an even shade Two coat applied @ 0.90 ltr/10 m² over an under coat of primer applied @ 0.80 ltr/10 m² of approved brand and manufacture including preparing the surface after thoroughly cleaning oil, grease, dirt and foreign matter, cost of materials, labour complete as per specifications and as per the direction of	Sqm	126.48	2.61	2	19-11-2022	26-11-2022	7
80	Providing, laying & fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick conforming to IS 1237 heavy duty tiles for flooring, treads of steps and landing, laid on a bed of 12mm thick cement mortar 1:3 mix finished with flush pointing using white cement, including cost of materials, mortar, including curing, grinding the	Cum	29.35	0.00	0	05-09-2022	31-01-2023	148
81	Providing Teak wood frames of doors, windows, clerestory windows, ventilators and other frames, wrought, framed or assembled including making glaster groves (excluding cost of cement concrete and side clamps), but including cost of materials, labour, usage charges complete as per specifications. and as per the direction of engineer incharge of work	Cum	0.11	0.00	0	05-09-2022	31-01-2023	148
82	Providing and fixing in position fully panelled Teak wood shutters for doors with stiles and rails of 40mm thick with bottom and lock rails 180mm wide top rail and stiles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, usage charges complete as per specifications. and as per the direction of engineer incharge of work	Sqm	1.89	0.00	0	05-09-2022	31-01-2023	148

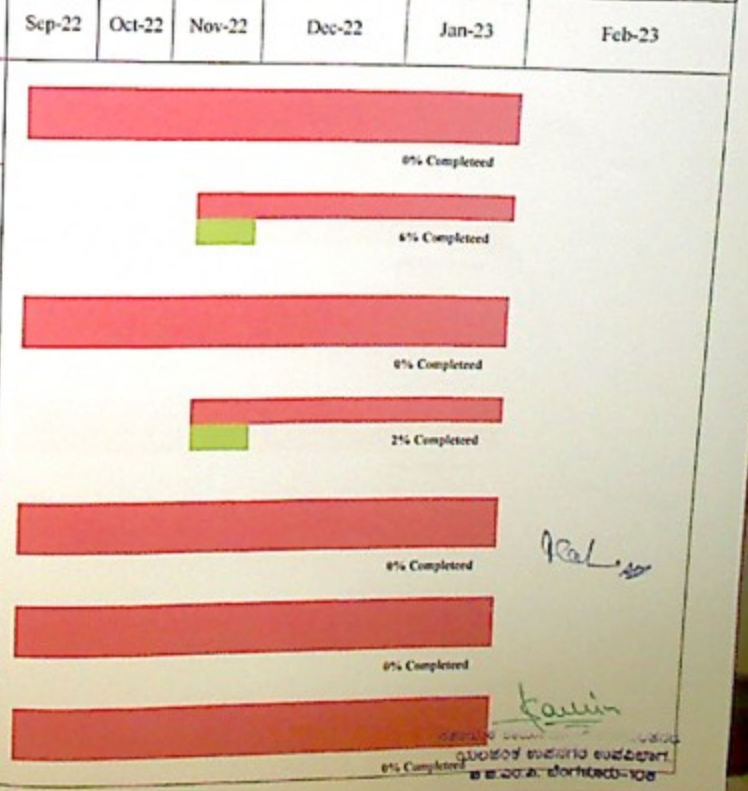

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
83	Polishing in high gloss/matt finish melamine clear polish on wood work in required color/wooden shade texture with following process in the sequence as detailed below 1 The surface to be polished is rubbed with sand paper 80/120 no. and then with sand paper of 160/180 nos. 2. Applying two coats of sealer with spray gun and allowing sufficient drying time for 1st coat and	Sqm	1 89	0.00	0	05-09-2022	31-01-2023	148
84	Supplying and fixing rolling shutters of approved make, made of required size M.S. laths, interlocked together through their entire length and jointed together at the end by end locks, mounted on specially designed pipe shaft with brackets, side guides and arrangements for inside and outside locking with push and pull operation complete, including the cost of providing and	Sqm	225.00	0.00	0	05-09-2022	31-01-2023	148
85	Providing & fixing of louvered ventilator made out of multi chambered UPVC(Matching to RAL-9016) sections and with minimum TiO2(Titanium Dioxide) at 6PHR with TPE(Thermo Plastic Elastomer) and lead free with gaskets -grey colour having isolated drainage and reinforced with Galvanized Iron profile through-out the ventilator frame. The frame having overall size of	Sqm	36.00	0.00	0	05-09-2022	31-01-2023	148
86	Applying priming coats with primer of approved brand and manufacture, having low VOC (Volatile Organic Compound) content. With water thinnable cement primer on wall surface having VOC content less than 50 grams/litre as per specifications and as per the direction of engineer incharge of work.	Sqm	113.79	0.00	0	05-09-2022	31-01-2023	148
87	Applying priming coats with primer of approved brand and manufacture, having low VOC (Volatile Organic Compound) content. With water thinnable cement primer on wall surface having VOC content less than 50 grams/litre as per specifications and as per the direction of engineer incharge of work.	Sqm	153.64	0.00	0	05-09-2022	31-01-2023	148
88	Design and Detailed Engineering supply and Erection of Structural Steel Support complete with 2 coat of epoxy primer coating and with necessary fixing transportation site supervision and commissioning of tensioned membrane structure including preparation of membrane shop drawings of PVC tensioned membraneRoof Structure consisting of Flying mast out of IS	Sqm	980.43	980.10	100	19-11-2022	26-11-2022	7
89	Construction of Embankment with approved materials deposited at site from roadway cutting and excavation from drain and foundation of other structures graded with desired compaction and as per the direction of engineer incharge of work.	Cum	34446.38	34446.38	100	10-11-2022	20-11-2022	10

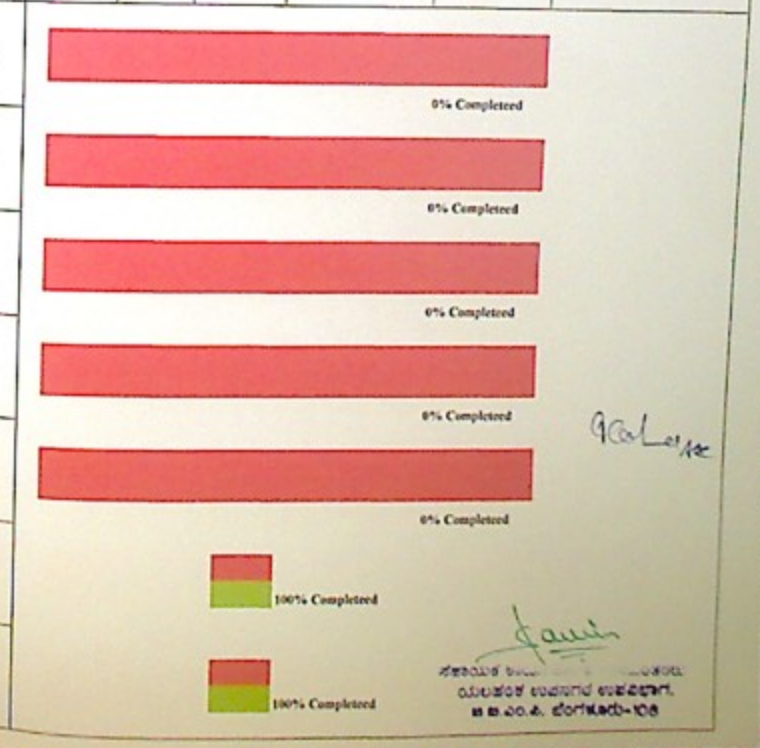

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
90	Construction of Embankment by excavating the available approved Gravel/Murrum deposited at a place or borrow pits during or prior excavation with all lifts and lead, transportation to site, spreading, grading to required slope and compacting to meet the requirement complete as per specifications, including cost of labour,rolling,water, all materials,usage& all	Cum	4395.33	4234.56	96	10-11-2022	20-11-2022	10
91	Providing and placing on terrace(at all floor levels), polyethylene water storage tanks as per IS 12701 marked,with cover and suitable locking arrangement and making necessary holes for inlet,outlet and overflow pipes but without fittings and the base support for tank(For 1000 Litre capacity) and as per the direction of engineer incharge of work.	lt	2000.00	2000.00	100	19-11-2022	26-11-2022	7
92	Providing and fixing stainless steel (Grade 304) railing made of Hollow tubes, channels, plates etc , including welding, grinding, buffing, polishing and making curvature (wherever required) and fitting the same with necessary stainless steel nuts and bolts complete, t/c fixing the railing with necessary accessories & stainless steel dash fasteners, stainless steel bolts	Kg	165.60	0.00	0	05-09-2022	31-01-2023	148
93	Providing and fixing stainless steel (Grade 304) railing made of Hollow tubes, channels, plates etc , including welding, grinding, buffing, polishing and making curvature (wherever required) and fitting the same with necessary stainless steel nuts and bolts complete, t/c fixing the railing with necessary accessories & stainless steel dash fasteners, stainless steel bolts	Sqm	165.60	0.00	0	05-09-2022	31-01-2023	148
94	Providing and laying Polished Granite stone flooring in required design and patterns, in linear as well as curvilinear portions of the building all complete as per the architectural drawings with 18 mm thick stone slab over 20 mm (average) thick base of cement mortar 1:4 (1 cement : 4 coarse sand) laid and jointed with cement slurry and pointing with white cement slurry admixed	Sqm	215.60	37.11	17	19-11-2022	26-11-2022	7
95	Providing and laying Polished Granite stone flooring in required design and patterns, in linear as well as curvilinear portions of the building all complete as per the architectural drawings with 18 mm thick stone slab over 20 mm (average) thick base of cement mortar 1:4 (1 cement : 4 coarse sand) laid and jointed with cement slurry and pointing with white cement slurry admixed	Sqm	102.97	0.00	0	05-09-2022	31-01-2023	148
96	Providing and fixing Steel work in built up tubular (round, square or rectangular hollow tubes etc) trusses etc , including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc complete. Electric resistance or induction butt welded tubes including cost of materials, labour,	Kg	11103.67	0.00	0	05-09-2022	31-01-2023	148

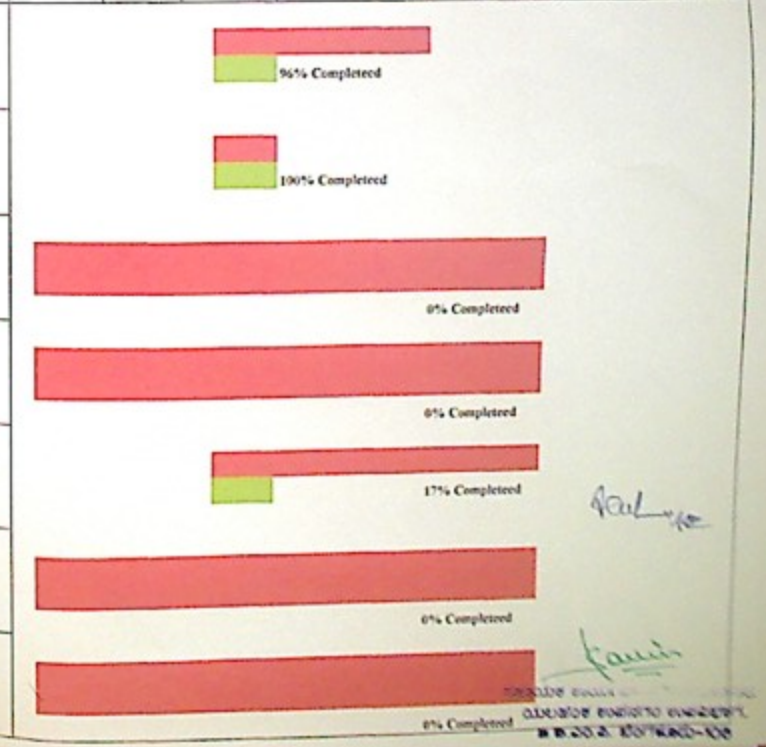

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-02-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No of Working Days
97	Providing and fixing PUF Panel with pre-coated galvanized iron profile sheets on flat top surface and a ribbed liner tray on the underside and a sandwiched insulation cover. The profile is a hi-flow liner sheet. Ribbed liner, minimum 0.5 mm gauge Outer skin 35x250mm trapezoidal profile with 3 secondary ribs and anti-capillary flute. The panel thickness of 50 mm. Surface Finish: Metallic, solid colours, Polyvinylidene fluoride (PVDF) & super polyster coatings. The Specifications of pre-coated galvanized iron profile sheets is as follows (size, shape and pitch of corrugation as approved by Engineer-in-	Sqm	583.96	0.00	0	05-09-22	31-01-23	148
98	Providing and fixing pre-coated galvanized steel sheet roofing accessories 0.50 mm (~0.65 %) total coated thickness, Zinc coating 120 grams per m2 as per IS: 277, in 240 mpa steel grade, 5+5 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling self tapping screws complete. Gutter (600 mm over all girth) and as per the direction of engineer incharge of work.	Rm	81.90	0.00	0	05-09-22	31-01-23	148
99	Providing & fixing flat iron brackets 50x3 mm size with necessary bolts, nuts and washers etc. for fixing G.S. sheets gutters with perlins. and as per the direction of engineer incharge of work..	Rm	81.90	0.00	0	05-09-22	31-01-23	148
100	Providing and fixing to wall, ceiling and floor unplasticised PVC 6.00 kgs/sqcm working pressure with pipe fittings, wall clips etc., and making good the wall, ceiling and floor for sanitary pipelines including cost of all materials,labour charges, HOM of equipments and testing complete as per specifications For Rain water pipe dn-110mm dia and as per the direction of engineer incharge of work.	Rm	12.00	0.00	0	05-09-22	31-01-23	148
101	Executive Bench Made out of Jadarahalli grey granite stone with hand supports with 3 line finishing with arch plain design with 100mm slabe height 60x Length 1500 width 450mm (1 SQ/C 45%) 50m (Including lead and I/S Charges) (inclusive of all taxes) As per the direction of Engineer Incharge. (Data approved rate)	Nos	42.00	0.00	0	05-09-22	31-01-23	148
102	Loading and Unloading of Stone Boulder Stone aggregate Sand Kachar Murram (Upper 5.5 m3) and as per the direction of engineer incharge of work.	Cum	13376.81	4508.44	34	10-09-22	20-10-22	71

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ ಉಪವಿಭಾಗ,
ಬ.ಬ.ಮ.ಪ. ಬೆಂಗಳೂರು-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
103	Cost of Haulage Excluding Loading and Unloading Taking output 10 t load and lead 10 km = 100 t km and as per the direction of engineer incharge of work	t Km	17119.76	5770.80	34	10-09-2022	20-11-2022	71
104	Concealed Conduit System Supplying heavy gauge PVC conduit pipe mm dia mm thick confirming to IS 2509 with suitable size bends, metal PVC junction boxes, adhesive paste etc., and running before concreting the slab. The conduit should be tied to the reinforcement rods by using binding wires and unused ways of junction boxes and pipe ends	Mtr	585.00	385.00	66	19-11-2022	26-11-2022	7
105	Concealed Conduit System Supplying heavy gauge PVC conduit pipe mm dia mm thick confirming to IS 2509 with suitable size bends, metal PVC junction boxes, adhesive paste etc., and running before concreting the slab. The conduit should be tied to the reinforcement rods by using binding wires and unused ways of junction boxes and pipe ends	Mtr	1125.00	825.00	73	19-11-2022	26-11-2022	7
106	Concealed Conduit System Supplying heavy gauge PVC conduit pipe mm dia mm thick confirming to IS 2509 with suitable size bends, metal PVC junction boxes, adhesive paste etc., and running before concreting the slab. The conduit should be tied to the reinforcement rods by using binding wires and unused ways of junction boxes and pipe ends	Mtr	170.00	85.00	50	19-11-2022	26-11-2022	7
107	Extra for Groove cutting in brick wall CC floor to the suitable depth for concealing of Conduit/GI pipe and plastering, finishing upto wall surface complete upto 50mm conduit in brick wall and as per the direction of engineer incharge of work	Mtr	200.00	25.00	13	19-11-2022	26-11-2022	7
108	Supplying and fixing of PVC casing and capping on the wall or ceiling using necessary materials like bends, screws at an interval of 300mm etc as required. 25mm and as per the direction of engineer incharge of work	Mtr	155.00	40.00	26	19-11-2022	26-11-2022	7
109	Supplying PVC/GI flexible conduit pipe mm dia fixing on surface over inverted tapered wooden plugs or phill plugs or rawl plugs and clamped using heavy gauge saddles at an interval of 300mm using NF screws and on either end of the pipe terminated completely 25mm complete and as per the directions of the Engineer-in-charge of the work.	Mtr	390.00	90.00	23	19-11-2022	26-11-2022	7

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23
110	Supplying And Fixing Metal Fan Box with Round Hook. and as per the direction of engineer incharge of work	Each	41.00	6.00	15	19-11-2022	26-11-2022	7			15% Completed			
111	Point wiring using Copper wire without switch. Supplying and wiring adopting loop system in existing PVC Conduit / casing capping using 1100V grade, COPPER conductor flexible multistrand FRLS PVC insulated, 2X1.55q mm Cable confirming to the GTP without switch, the other end of the wires shall be terminated with sufficient loose length in a	Each	137.00	9.00	7	19-11-2022	26-11-2022	7			7% Completed			
112	Medium point above 3Mtr upto 6Mtr from tapping point to out let via switch box. and as per the direction of engineer incharge of work.	Each	17.00	14.00	82	19-11-2022	26-11-2022	7			82% Completed			

Goal

Executive Engineer
Yelahanka Division
B.B.M.P. Bengaluru-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross r Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division ur Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
113	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade, multistrand Copper with low conductor resistance single core wire in open or concealed system of wiring with specified IS-694 1990 & confirming to GTP of GROUP -A 1.5 sqmm and as per the direction of engineer incharge of work.	Mtr	1725.00	775.00	45	19-11-2022	26-11-2022	7
114	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade, multistrand Copper with low conductor resistance single core wire in open or concealed system of wiring with specified IS-694 1990 & confirming to GTP of GROUP -A 2.5 sqmm and as per the direction of engineer incharge of work.	Mtr	2480.00	1680.00	68	19-11-2022	26-11-2022	7
115	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade, multistrand Copper with low conductor resistance single core wire in open or concealed system of wiring with specified IS-694 1990 & confirming to GTP of GROUP -A 4 sqmm and as per the direction of engineer incharge of work.	Mtr	290.00	200.00	69	19-11-2022	26-11-2022	7
116	Supplying and flush mounting powder coated / galvanized metal box suitable for mounting modular switch plates. The box should be firmly flush mounted after due groove cutting in Brick/Stone/C.C wall 1-3Way and as per the direction of engineer incharge of work.	Each	71.00	21.00	30	19-11-2022	26-11-2022	7
117	Supplying and flush mounting powder coated / galvanized metal box suitable for mounting modular switch plates. The box should be firmly flush mounted after due groove cutting in Brick/Stone/C.C wall 6Way and as per the direction of engineer incharge of work.	Each	50.00	15.00	30	19-11-2022	26-11-2022	7
118	Supplying and flush mounting powder coated / galvanized metal box suitable for mounting modular switch plates. The box should be firmly flush mounted after due groove cutting in Brick/Stone/C.C wall 8Way and as per the direction of engineer incharge of work.	Each	8.00	8.00	100	19-11-2022	26-11-2022	7

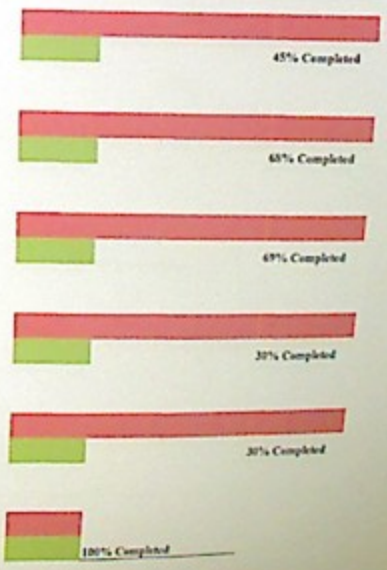

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross ro Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division ur Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-2022
Project End Date	:	03-02-2023
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23
119	Supplying and flush mounting powder coated / galvanized metal box suitable for mounting modular switch plates. The box should be firmly flush mounted after due groove cutting in Brick/Stone/C C wall 10-12Way and as per the direction of engineer incharge of work.	Each	48.00	10.00	21	19-11-2022	26-11-2022	7				21% Completed	
120	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos of machine screws, bolts nuts etc , complete on the existing metal/PVC box 1 to 3 Module. and as per the direction of engineer incharge of work.	Each	65.00	15.00	23	19-11-2022	26-11-2022	7				23% Completed	
121	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos of machine screws, bolts nuts etc , complete on the existing metal/PVC box 6 Module. and as per the direction of engineer incharge of work.	Each	20.00	20.00	100	19-11-2022	26-11-2022	7				100% Completed	
122	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos of machine screws, bolts nuts etc , complete on the existing metal/PVC box 8 Module. and as per the direction of engineer incharge of work.	Each	34.00	20.00	59	19-11-2022	26-11-2022	7				59% Completed	
123	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos of machine screws, bolts nuts etc , complete on the existing metal/PVC box12 Module. and as per the direction of engineer incharge of work.	Each	26.00	12.00	46	19-11-2022	26-11-2022	7				46% Completed	

GBL

executive engineer yelahanka
division bruhat bengaluru
mahanagara palike

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-02-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
124	Supplying and fixing of modular switch/ Socket/stepped electronic fan regulator/ dimmer/telephone socket etc on existing modular switch plate as per IS 3854 and IS 1293 GROUP A 6Amps one way and as per the direction of engineer incharge of work.	Each	19.00	9.00	47	19-11-22	26-11-22	7
125	Supplying and fixing of modular switch/ Socket/stepped electronic fan regulator/ dimmer/telephone socket etc on existing modular switch plate as per IS 3854 and IS 1293 GROUP A 6Amps Two way and as per the direction of engineer incharge of work.	Each	5.00	5.00	100	19-11-22	26-11-22	7
126	Stepped Fan Regulator and as per the direction of engineer incharge of work.	Each	3.00	3.00	100	19-11-22	26-11-22	7
127	16Amps one way switch. and as per the direction of engineer incharge of work.	Each	7.00	7.00	100	19-11-22	26-11-22	7
128	TV/Telephone socket. and as per the direction of engineer incharge of work.	Each	1.00	1.00	100	19-11-22	26-11-22	7
129	Supplying 50mm wooden plug, tapered from 50x50mm to 25x25mm and fixing by using binding wire before concreting a roof slab and as per the direction of engineer incharge of work.	Mtr	111.00	111.00	100	19-11-22	26-11-22	7
130	Supplying and fixing cast Aluminium round or oblong type bulk head fitting with GI wire guard, glass cover with 15Watts 230V CFL lamp and as per the direction of engineer incharge of work.	Each	5.00	5.00	100	19-11-22	26-11-22	7

9/12

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಾರ್ಯಾಲಯದ
ಯಲಹಂಕ ವಿಭಾಗದ ಅಭಿವೃದ್ಧಿ
ಬ.ಬ.ಮ.ಪ. ಬೆಂಗಳೂರು-106

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-02-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
131	Supplying CFL mirror light fitting with 8x11W CFL lamp, choke, Perspex cover and completely wired for use on 230V 50Hz AC supply and as per the direction of engineer incharge of work.	Each	24.00	24.00	100	19-11-22	26-11-22	7
132	LED Indoor Supplying of 2' feet - LED PVC Square Button W with high quality diffuser with Life of 25000 burning hours & 70% lumen maintenance with CRI > 80. Power Input: 220-240V @ 50Hz & Power factor >0.9 along with CE approved drivers. 5 years Warranty against any manufacturing defect working under standard electrical condition LED	Each	91.00	15.00	16	19-11-22	26-11-22	7
133	Supply of recess mounted ceiling type LED square or round Down light 12 watts with 4/5W GU 10 LED Lamp Rib Fabricated from Die cast aluminum with white powder coated prewired to mains connector with suitable driver & having swiveling unit of aluminum die cast eye ball & LED Lamp position retained by circular wire spring. 5 years Warranty	Each	24.00	24.00	100	19-11-22	26-11-22	7
134	Supply of LED Square Recessed Down lighters with 18W System Wattage Housing shall be with powder coated pressure die cast aluminum alloy with corrosion resistant polyester powder coat & with extended heat sink. Diffuser/cover made of Lexan plastic material. Rated life shall be L70 @ 50000 Hrs. which shall has inbuilt electrical protection like overlander	Each	15.00	15.00	100	19-11-22	26-11-22	7
135	60W highbay LED luxeat type light fixture make-easergion ,model - LHBL60CDL and as per the direction of engineer incharge of work.	Each	104.00	104.00	100	19-11-22	26-11-22	7
136	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' Type curve, indicator ON/OFF, energy cross-3 with Short circuit breaking capacity of 10K and complete wiring as required confirming to IEC 60898. 5-32Amps SP and as per the direction of engineer incharge of work	Each	6.00	6.00	100	19-11-22	26-11-22	7
137	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' Type curve, indicator ON/OFF, energy cross-3 with Short circuit breaking capacity of 10K and complete wiring as required confirming to IEC 60898. 5-32Amps SP and as per the direction of engineer incharge of work.	Each	7.00	5.00	71	19-11-22	26-11-22	7

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: Construction of Synthetic tennis court,street vending zone & other developmental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	: Rudraprasad Consultants
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 03-09-22
Project End Date	: 03-02-23
Project Length in Months	: 6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
138	40-63Amps DP and as per the direction of engineer incharge of work.	Each	6.00	6.00	100	19-11-22	26-11-22	7
139	40-63Amps TPN. and as per the direction of engineer incharge of work.	Each	2.00	2.00	100	19-11-22	26-11-22	7
140	Supplying and fixing regular MCB distribution boards on wall / wood board / flush mounting using required clamps, bolts, nuts etc . with provision for fixing suitable type capacity MCB's single phase / 3 phase / single door with powder coated painting. Made out of 14 SWG MS enclosure II - Double Door 12Way SP &N. and as per the direction of	Each	29.00	2.00	7	19-11-22	26-11-22	7
141	Supplying and fixing regular MCB distribution boards on wall / wood board / flush mounting using required clamps, bolts, nuts etc . with provision for fixing suitable type capacity MCB's single phase / 3 phase / single door with powder coated painting. Made out of 14 SWG MS enclosure III - Double Door 4Way TP &N. and as per the direction of	Each	1.00	1.00	100	19-11-22	26-11-22	7
142	Supplying, fixing and wiring Earth Leakage Miniature Circuit Breaker (ELMCB) 240/415V up to 300mA sensitivity on existing wood/panel board. 32-40 Amps 2 pole and as per the direction of engineer incharge of work.	Each	4.00	2.00	50	19-11-22	26-11-22	7
143	Supplying and running of GI/Copper strips for grounding connections, using necessary fixing materials as required. GI strip 25x3mm and as per the direction of engineer incharge of work.	Each	4.00	2.00	50	19-11-22	26-11-22	7
144	Supplying fixing and wiring earth electrode for grounding of lifts, transformers, DG sets etc, using 40mm dia 2.9mm thick 2.5 mtr long GI pipe with GI funnel with mesh and suitable size reducer fixed on the top of the earth electrode. The funnel should be enclosed in a CC chamber of 400x400x400mm with a cast iron cover. The earth electrode shall have	Mtr	10.00	10.00	100	19-11-22	26-11-22	7
145	Fabricating supplying and mounting MS box made out 5WG suitable for floor / wall mounting, fully weather proof with provision for better heat dissipation, provided with hinged front cover, equipped with tamper proof locking arrangements, with suitable size clamps with necessary cable entry pipe with gland and box should be finished with 2 coats of red oxide	Sq Cms	150000.00	150000.00	100	19-11-22	26-11-22	7
146	600x600x3mm GI Plate and as per the direction of engineer incharge of work.	Each	2.00	2.00	100	19-11-22	26-11-22	7

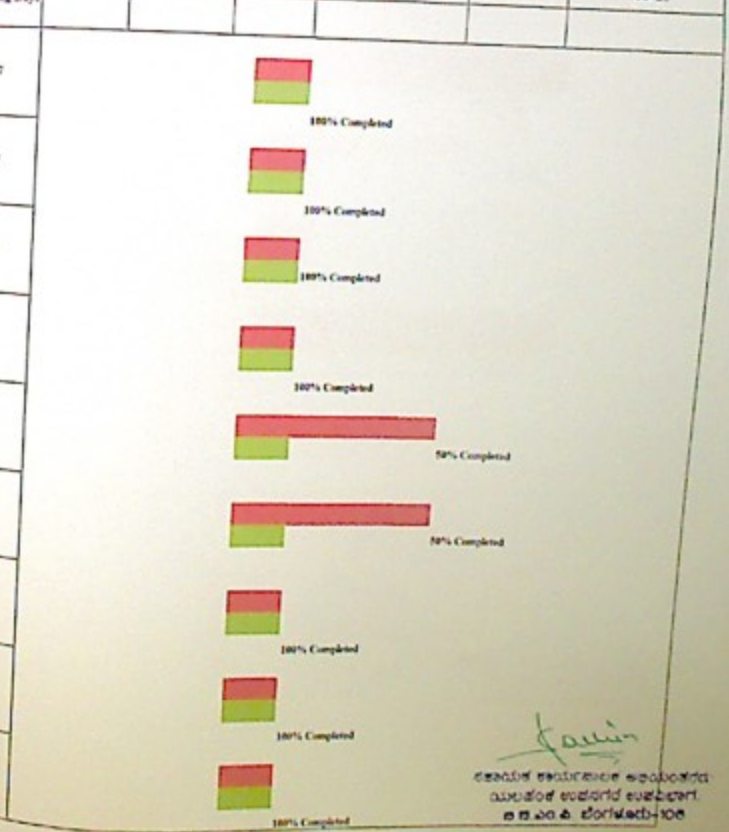

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of Synthetic tennis court,street vending zone & other developemental works at judicial layout main and cross roads, Chikkabommasandra, Someshwara nagar,Allalasandra village & surrounding areas in ward No-04 of yelahanka Division under Amruth Nagarothan Grants. (Package No-06)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Reehan
Project Start Date	:	03-09-22
Project End Date	:	03-02-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
147	Supplying and fixing of modular switch & connected accessories on existing modular switch plate as per IS 3854 and IS 1293 6 A Two Way Switch and as per the direction of engineer incharge of work.	Each	310.00	0.00	0	05-09-22	31-01-23	148
148	Supplying capacitor type ceiling fan complete with down rod blades shackle, canopies etc. for operation on 230 volts, 50 cycles, single phase AC supply conforming to ISS-374-1979 and with double ball bearing systems 48" sweep (1200mm) and as per the direction of engineer incharge of work.	Each	9.00	1.00	11	19-11-22	26-11-22	7
149	Supplying and fixing of slim putty fitting, made out of CRCA Sheet metal body with locking type holder completely wired Excluding Ballast & Fluorescent Tube and as per the direction of engineer incharge of work.	Each	2.00	2.00	100	19-11-22	26-11-22	7
150	Supplying exhaust fan of 1440 RPM of 300 mm (12") size with bracket blades complete for light duty suitable to operate on 230V 50Hz. AC Supply and as per the direction of engineer incharge of work.	Each	25.00	0.00	0	05-09-22	31-01-23	148

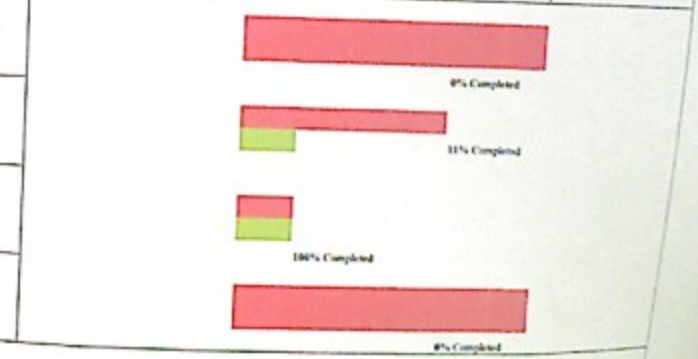

RVBC

RUDRAPRASAD CONSULTANTS BANGALORE
